

2020 Mesa Moves Bond Program Update

Transportation Advisory Board
July 21, 2026

Sabine King, P.E.
Assistant Transportation Director



On November 3, 2020, Mesa voters authorized the City of Mesa to issue \$100M of General Obligation Bonds to fund transportation projects throughout the City

2020 Mesa Moves Bond Program Summary

$$\text{\$100M} + \text{\$62M} = \text{\$162M}$$

*City of Mesa
General Obligation
Street Bond*

*Maricopa Association of
Governments (MAG)
Funding*

*Total Available Funds
For Transportation Projects*


2020 Mesa Moves Bond Program Project Costs

Price Increase since 2020

- Materials
- Labor
- Real Estate

Actions Taken

- Prioritize projects based on need and reimbursement
- Work with MAG to maximize reimbursements
- Used additional funding from Transportation Funds
- Place some projects on hold

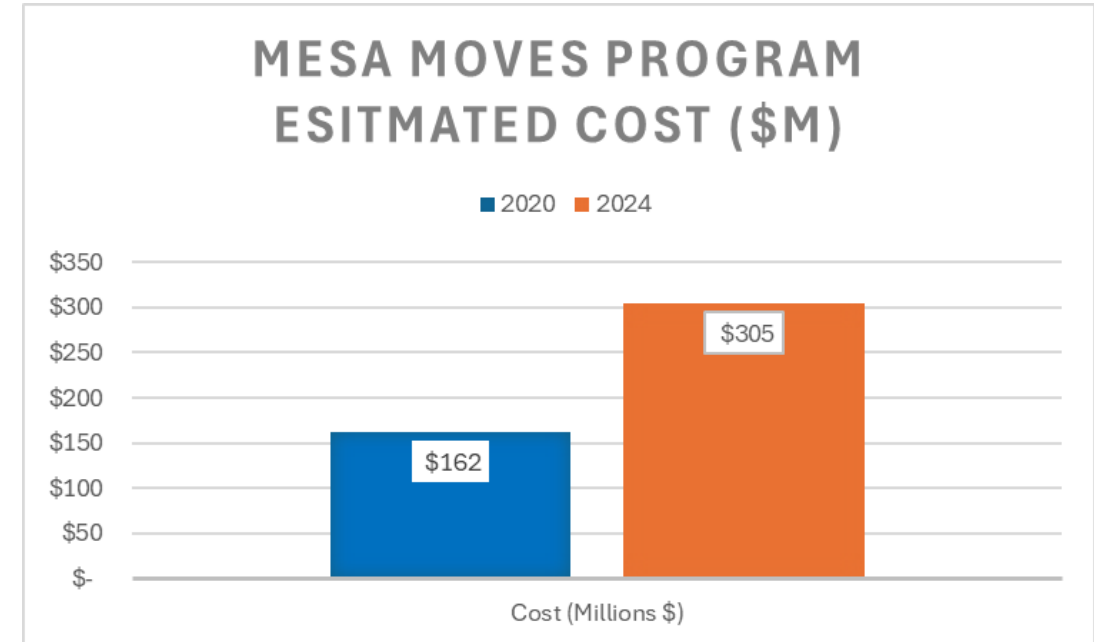

Mesa Moves Project Status



Regional Roadway Improvements

<u>Project</u>	<u>Status</u>
1. Signal Butte Road – Williams Field Road to Germann Road	Completed
2. Sossaman Road and Baseline Road	Completed
3. Williams Field Road & Ellsworth Road	Completed
4. Sossaman Road – Ray Road to Warner Road	Completed
5. Broadway Road – Mesa Drive to Stapley Drive	Under Construction (ETA Spring 2028)
6. Ray Road Connection to Ellsworth Road	Under Construction (ETA Fall 2026)
7. Val Vista Drive – US 60 to Pueblo Avenue	Under Construction (ETA Spring 2027)
8. Ellsworth Road – Germann Road to Ray Road	Under Construction (ETA Spring 2027)
9. Elliot Road – Sossaman Road to Ellsworth Road	Final Design (Construction Fall 2026)
10. Stapley Drive & University Drive	60% Design – On Hold, No Funding



Arterial Roadway Reconstruction

Project

1. Southern Avenue – Gilbert Road to Val Vista Drive
2. Greenfield Road – Southern Avenue to Main Street
3. Greenfield Road – Main Street to Adobe Road
4. Country Club Drive & Southern Avenue
5. Broadway Road – Stapley Drive to Gilbert Road
6. Broadway Road – Country Club Drive to Mesa Drive
7. University Drive – Mesa Drive to Harris Drive
8. Stapley Drive – University Drive to McKellips

Status

Completed

Completed

Completed

Design 2020 Bond/Construction Other Funding

No Funding - 2026 Bond


No Funding

No Funding

No Funding



Arterial Roadway Reconstruction

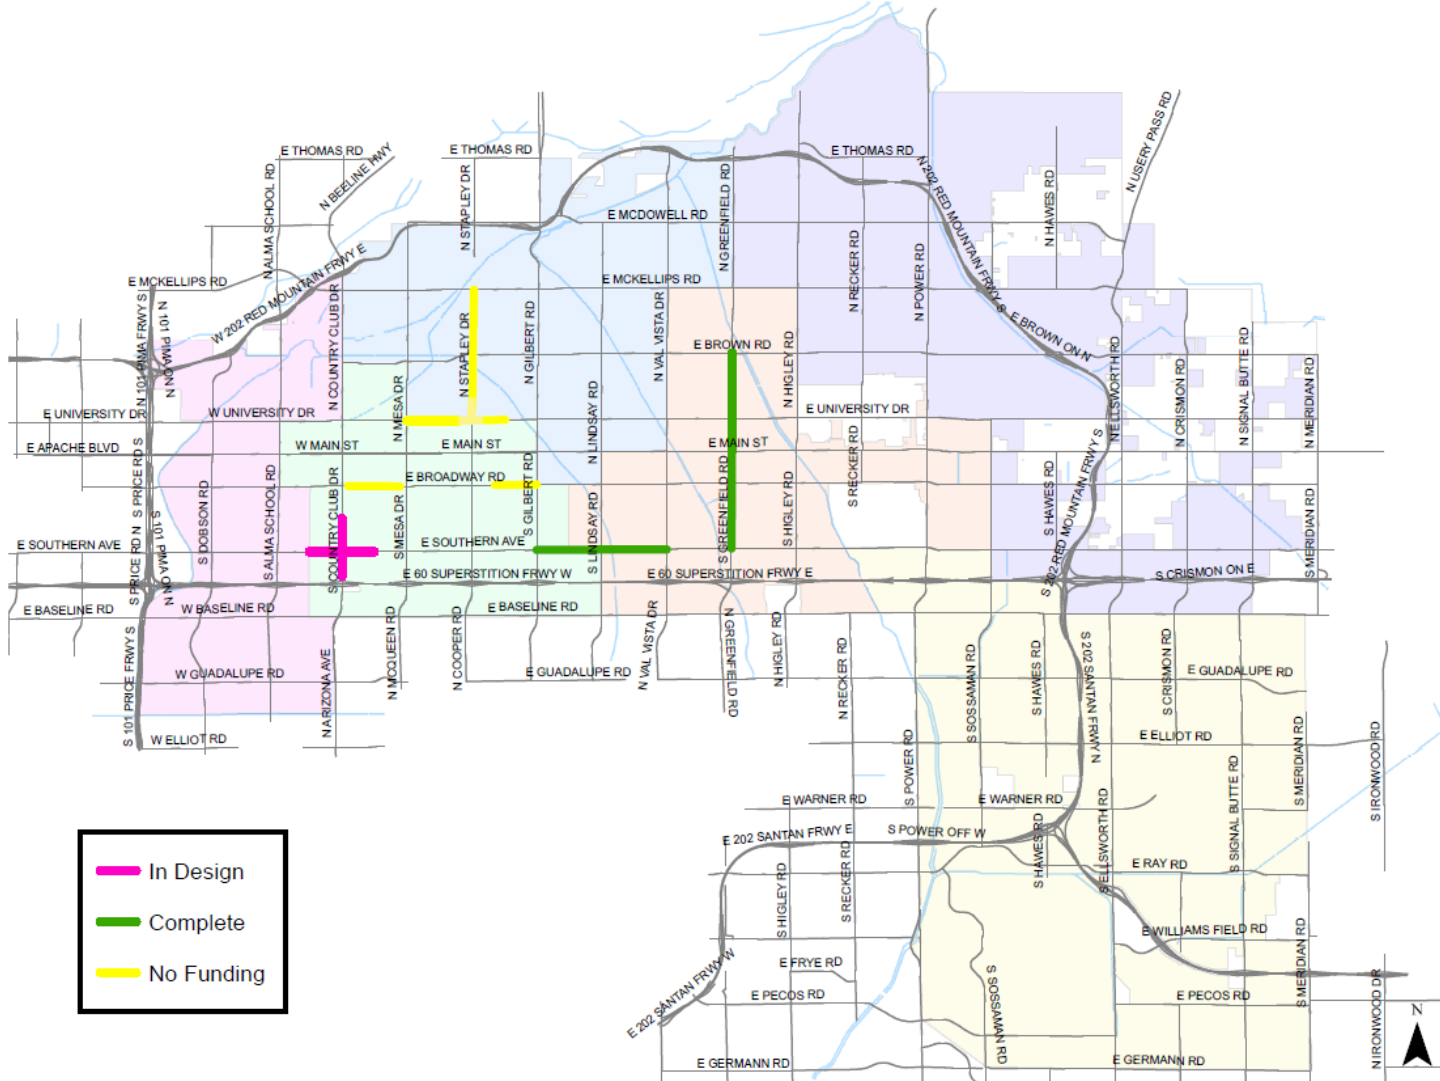

Active Transportation

Project


1. Lehi Loop SUP Phase 2 Feasibility Study
2. Center Street - Brown Road to Broadway Road Feasibility Study
3. Eastern Canal – Brown Road to Broadway Road
4. Eastern Canal – Broadway Road to Baseline
5. US 60 Consolidated Canal to Eastern Canal
6. Mesa Gateway Phase 3

Status

- Completed - Final Report 12/2023
- Completed - Final Report 04/2024
- Construction in Spring 2027
- Construction in Winter 2026
- 75% Design 2020 Bond/Construction 2026 Bond
- No Funding - 2026 Bond



Active Transportation Projects

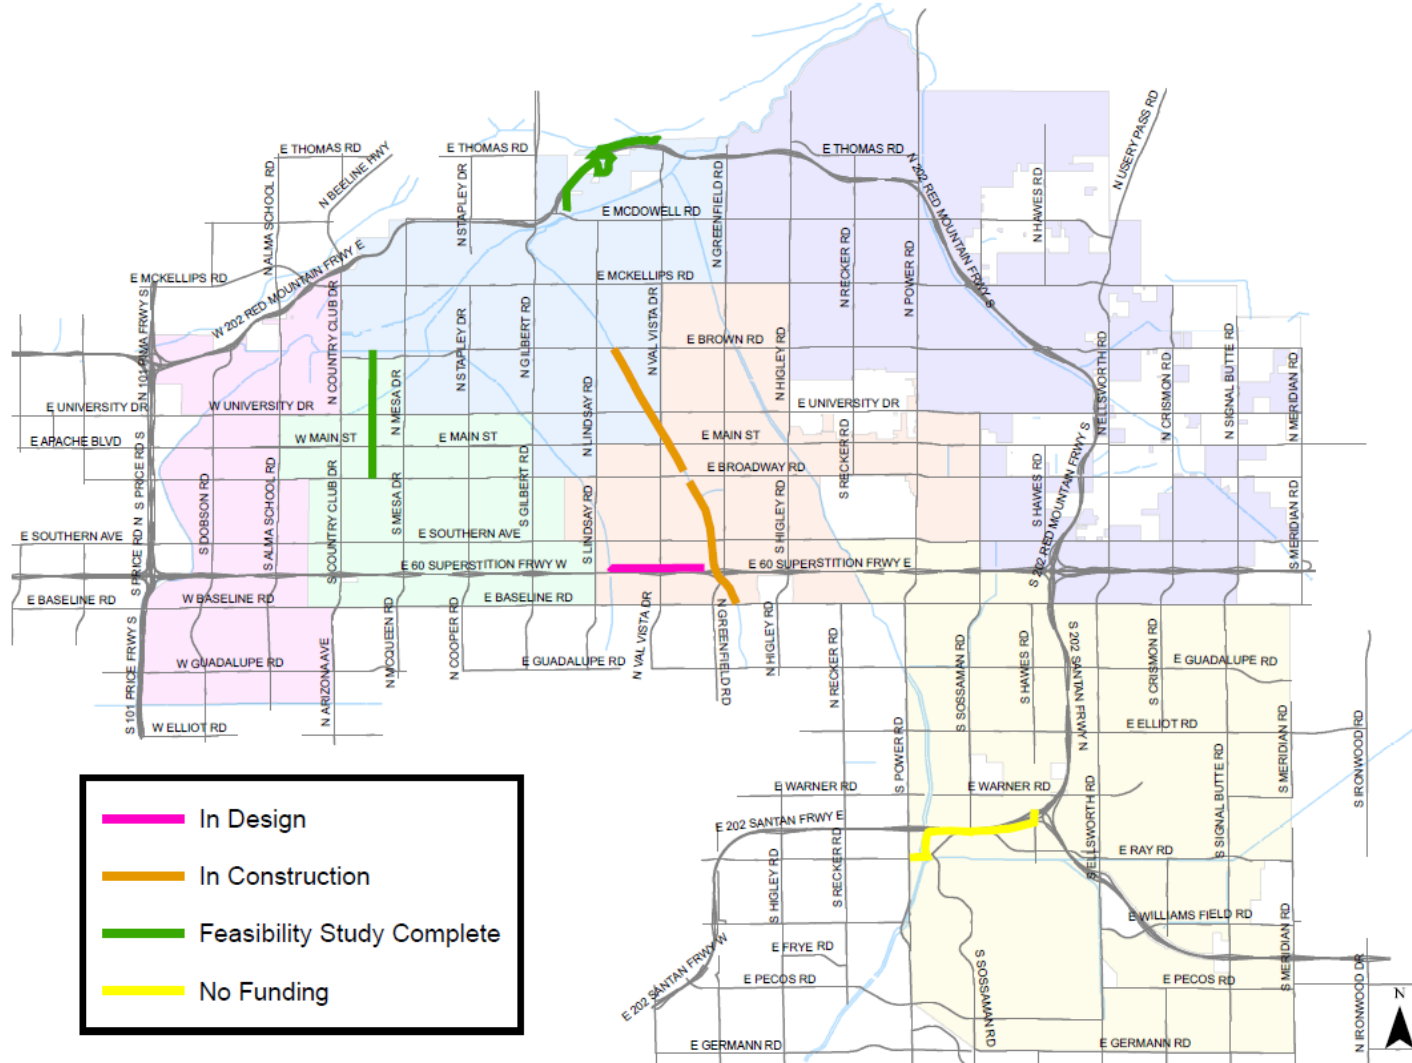

2026 Transportation Bond




Transportation Safety Project Summary

	2026 Transportation Safety Bonds	2026 Bond Amount	Other Funding	Total Project Cost	Status
1	Warner Road Bridge	\$ 16,847,534	\$ 21,377,042	\$ 38,224,576	
2	Mesa Dr: Phase 3 Main to Brown	\$ 19,811,485	\$ 30,982,355	\$ 50,793,840	
3	AR - Broadway: Spur to Gilbert Rd	\$ 8,151,104		\$ 8,151,104	
4	Broadway: Stapley Dr to Gilbert Rd (raised medians)	\$ 10,632,720		\$ 10,632,720	Comprehensive Safety Action Plan
5	Downtown Multimodal Pathway	\$ 12,050,816		\$ 12,050,816	Concepts
6	Lehi Phase II and Nodes	\$ 12,924,864		\$ 12,924,864	Design
7	Mesa Gateway Phase III SUP	\$ 11,755,640		\$ 11,755,640	
8	US60 SUP: Eastern to Consolidated	\$ 12,993,720		\$ 12,993,720	Under Design
9	Higley: McKellips Rd to Broadway Rd (raised medians)	\$ 10,386,624		\$ 10,386,624	Comprehensive Safety Action Plan
10	Thomas Rd Multimodal	\$ 16,957,200		\$ 16,957,200	Concept Study
	Bond Issuance	\$ 1,500,000		\$ 1,500,000	
		\$ 134,011,707	\$ 52,359,397	\$ 186,371,104	

Source: Council Presentation May 14, 2026

2026 Bond Election

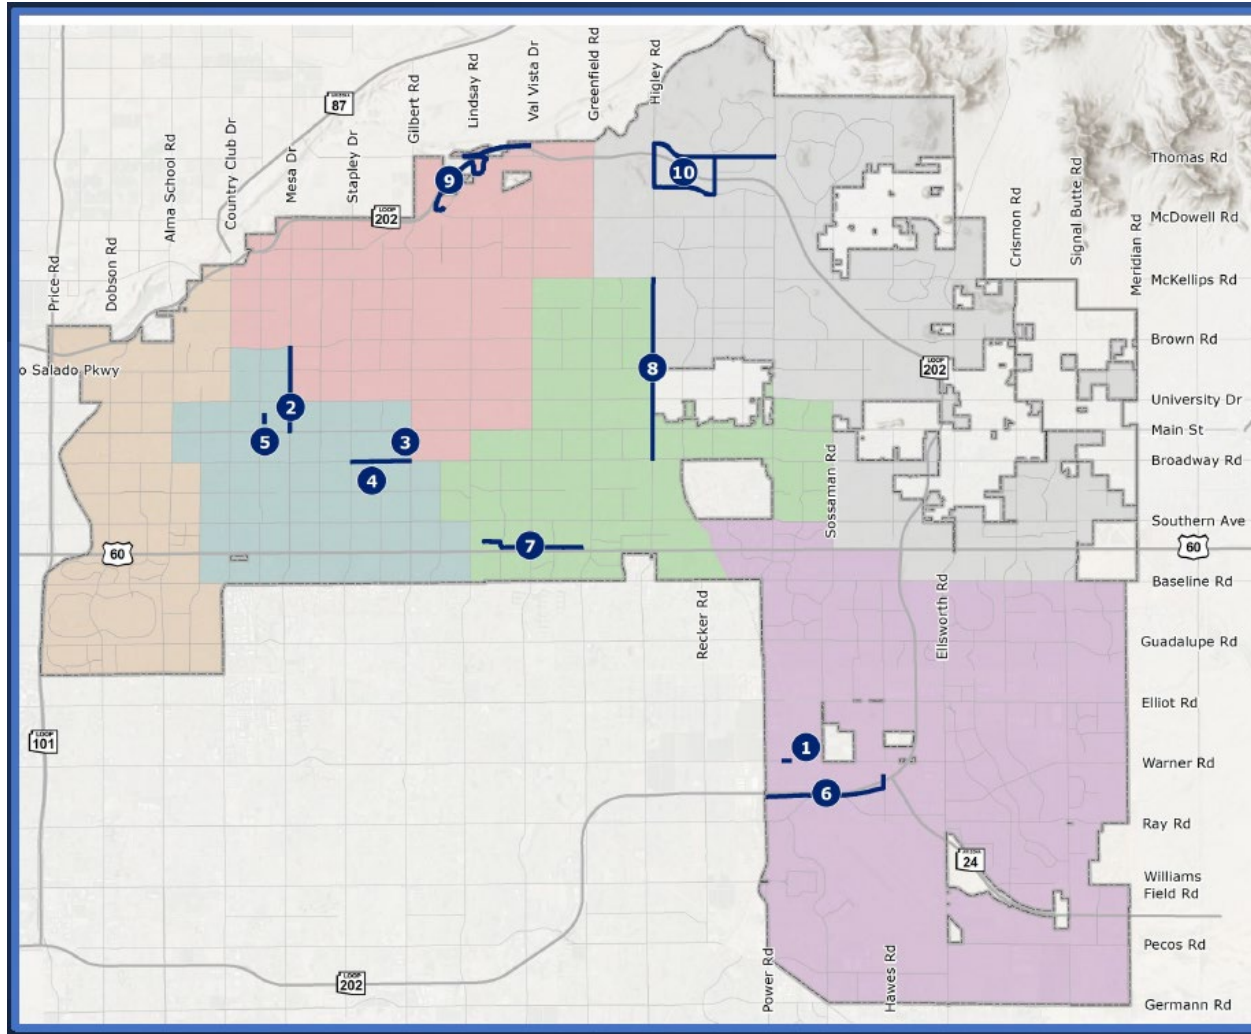

Source: Council Presentation May 14, 2026

Questions?



MESA MOVES

CONNECTING PEOPLE TO PLACES
